












































ID	Informasjon	Aktivitetstype	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	Navn på ressurser	
1			R81 Vaktmesterentreprisen	20 dager	ma 27.01.25	fr 21.02.25			47
2			Portørstue	20 dager	ma 27.01.25	fr 21.02.25			
3			Eierskifte BH leveranser modulbygg tak C	0 dager	fr 31.01.25	fr 31.01.25			
4			R82 Sengeposter og akuttmottak E3/E4	73 dager	ma 25.11.24	on 05.03.25			
5			HLK	12 dager	fr 29.11.24	ma 16.12.24			
6			Eierskifte	0 dager	fr 29.11.24	fr 29.11.24			
7			Innflytting	2 dager	fr 13.12.24	ma 16.12.24			
8			Akuttmottak og M. etg.	72 dager	ma 25.11.24	on 05.03.25			
9			Ferdigstilling og idriftsettelse	15 dager	ma 25.11.24	fr 13.12.24			
10			Eierskifte	0 dager	on 15.01.25	on 15.01.25			
11			Innflytting	0 dager	on 05.03.25	on 05.03.25			
12			Utomhus	73 dager	ma 25.11.24	on 05.03.25			
13			Bygging og idriftsettelse	50 dager	ma 25.11.24	fr 31.01.25			
14			Eierskifte	0 dager	ma 03.03.25	ma 03.03.25	13		
15			Innflytting	0 dager	on 05.03.25	on 05.03.25	14AS+3 dager		
16			Eventuell - Sengeoppstilling	0 dager	ma 25.11.24	ma 25.11.24			
17			Bygging, Finansiering						
18			R83 Sengeposter C2 og C4	59 dager	ti 17.12.24	fr 07.03.25			
19			C2	32 dager	ti 17.12.24	on 29.01.25			
20			Oppstart og riving	4 dager	ti 17.12.24	fr 20.12.24	7		
21			Bygging og idriftsettelse	14 dager	ma 06.01.25	to 23.01.25	20AS+10 dager		
22			Virksomhetstester	2 dager	fr 24.01.25	ma 27.01.25	21		

Prosjekt: Overordnet tidsplan re
Dato: to 23.01.25

Aktivitet		Inaktivt sammendrag		Eksterne aktiviteter	
Deling		Manuell aktivitet		Ekstern milepæl	
Milepæl		Bare varighet		Tidsfrist	
Sammendrag		Manuell sammendragsfremheving		Fremdrift	
Prosjektsammendrag		Manuelt sammendrag		Manuell fremdrift	
Inaktiv aktivitet		Bare start			
Inaktiv milepæl		Bare slutt			

ID		Aktivitetstype	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	Navn på ressurser	47
23			Eierskifte	0 dager	ti 28.01.25	ti 28.01.25	22		
24			Innflytting	2 dager	ti 28.01.25	on 29.01.25	23		
25			C4	27 dager	to 30.01.25	fr 07.03.25			
26			Oppstart og riving	4 dager	to 30.01.25	ti 04.02.25	24		
27			Bygging og idriftsettelse	19 dager	on 05.02.25	ma 03.03.25	26		
28			Virksomhetstester	2 dager	ti 04.03.25	on 05.03.25	27		
29			Eierskifte	1 dag	to 06.03.25	to 06.03.25	28		
30			Innflytting	1 dag	fr 07.03.25	fr 07.03.25	29		
31			R85 B2 prøvetaking og hovedinngang	99 dager	ma 25.11.24	to 10.04.25			
32			Prøvetaking	71 dager	ma 25.11.24	ma 03.03.25			
33			Bygging og idriftsetting	68 dager	ma 25.11.24	on 26.02.25			
34			Virksomhetstester	2 dager	to 27.02.25	fr 28.02.25	33		
35			Eierskifte	0 dager	fr 28.02.25	fr 28.02.25	34		
36			Innflytting	1 dag	ma 03.03.25	ma 03.03.25	35		
37			Hovedinngang - bygging og idriftsetting	99 dager	ma 25.11.24	to 10.04.25			
38			Bygging og idriftsetting	97 dager	ma 25.11.24	ti 08.04.25			
39			Eierskifte	0 dager	ti 08.04.25	ti 08.04.25	38		
40			Innflytting (når forplass 2 er ferdig)	2 dager	on 09.04.25	to 10.04.25	39		
41			R86 Klinisk forskningspost	70 dager	ma 25.11.24	fr 28.02.25			
42			Bygging og idriftsetting	36 dager	ma 06.01.25	ma 24.02.25			
43			Virksomhetstester	2 dager	ti 25.02.25	on 26.02.25	42		
44			Eierskifte	0 dager	ma 24.02.25	ma 24.02.25	42		


Prosjekt: Overordnet tidsplan re
Dato: to 23.01.25

Aktivitet		Inaktivt sammendrag		Eksterne aktiviteter	
Deling		Manuell aktivitet		Ekstern milepæl	
Milepæl		Bare varighet		Tidsfrist	
Sammendrag		Manuell sammendragsfremheving		Fremdrift	
Prosjektsammendrag		Manuelt sammendrag		Manuell fremdrift	
Inaktiv aktivitet		Bare start			
Inaktiv milepæl		Bare slutt			

ID	Aktivitetstype	Aktivitetsnavn	Varighet	Start	Slutt	Foregående aktiviteter	Navn på ressurser	
45		Innflytting	2 dager	to 27.02.25	fr 28.02.25	43		47
46		Eventuell	0 dager	ma 25.11.24	ma 25.11.24			
47		Rom for mikroskopering						
48		Rom for utstyr til endokrinologisk						
49		R88 Modulbygg C7 - foreldreovernatting	15 dager	ma 25.11.24	ma 16.12.24			
50		Bygging og idriftssetting	15 dager	ma 25.11.24	fr 13.12.24			
51		Igangsetting av leieforhold	0 dager	ma 16.12.24	ma 16.12.24	50		


Prosjekt: Overordnet tidsplan re
Dato: to 23.01.25

Aktivitet		Inaktivt sammendrag		Eksterne aktiviteter	
Deling		Manuell aktivitet		Ekstern milepæl	
Milepæl		Bare varighet		Tidsfrist	
Sammendrag		Manuell sammendragsfremheving		Fremdrift	
Prosjektsammendrag		Manuelt sammendrag		Manuell fremdrift	
Inaktiv aktivitet		Bare start			
Inaktiv milepæl		Bare slutt			

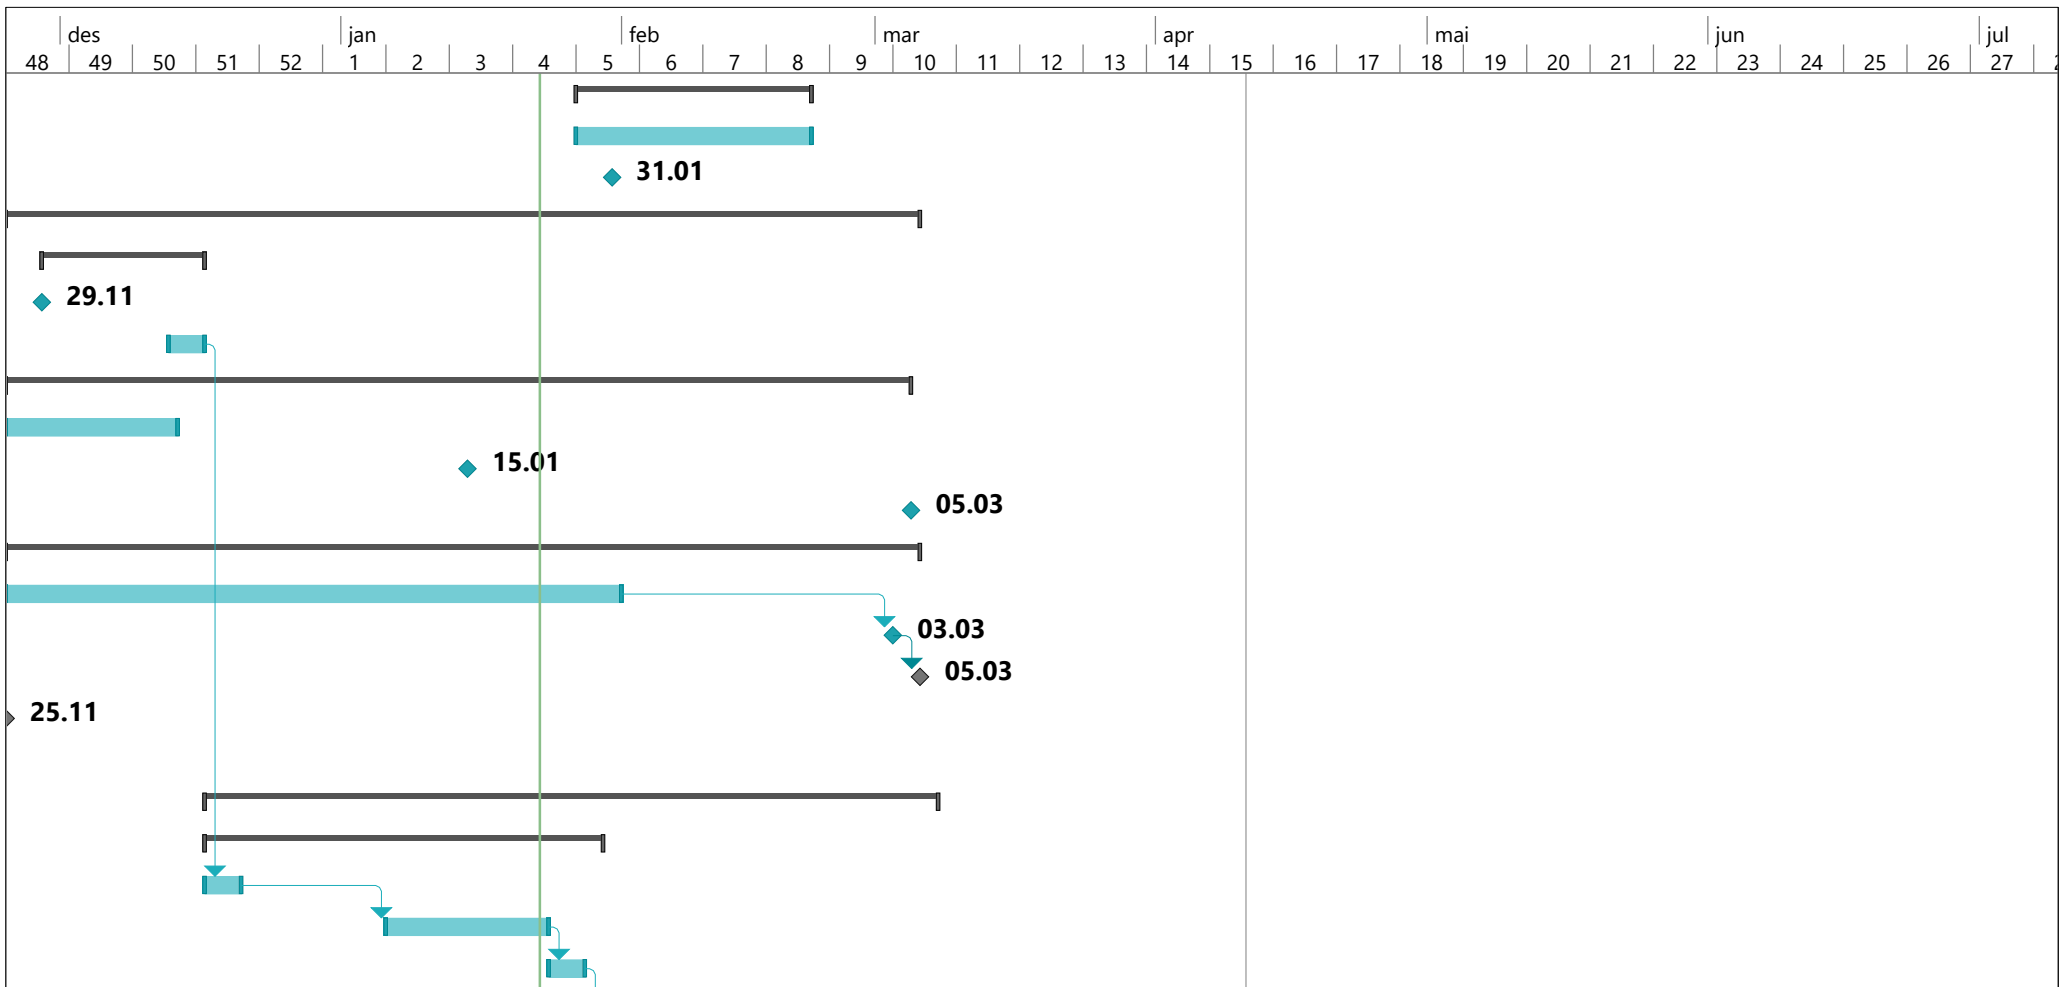


Prosjekt: Overordnet tidsplan re
 Dato: to 23.01.25

Aktivitet		Inaktivt sammendrag		Eksterne aktiviteter	
Deling		Manuell aktivitet		Ekstern milepæl	
Milepæl		Bare varighet		Tidsfrist	
Sammendrag		Manuell sammendragsfremheving		Fremdrift	
Prosjektsammendrag		Manuelt sammendrag		Manuell fremdrift	
Inaktivt aktivitet		Bare start			
Inaktivt milepæl		Bare slutt			

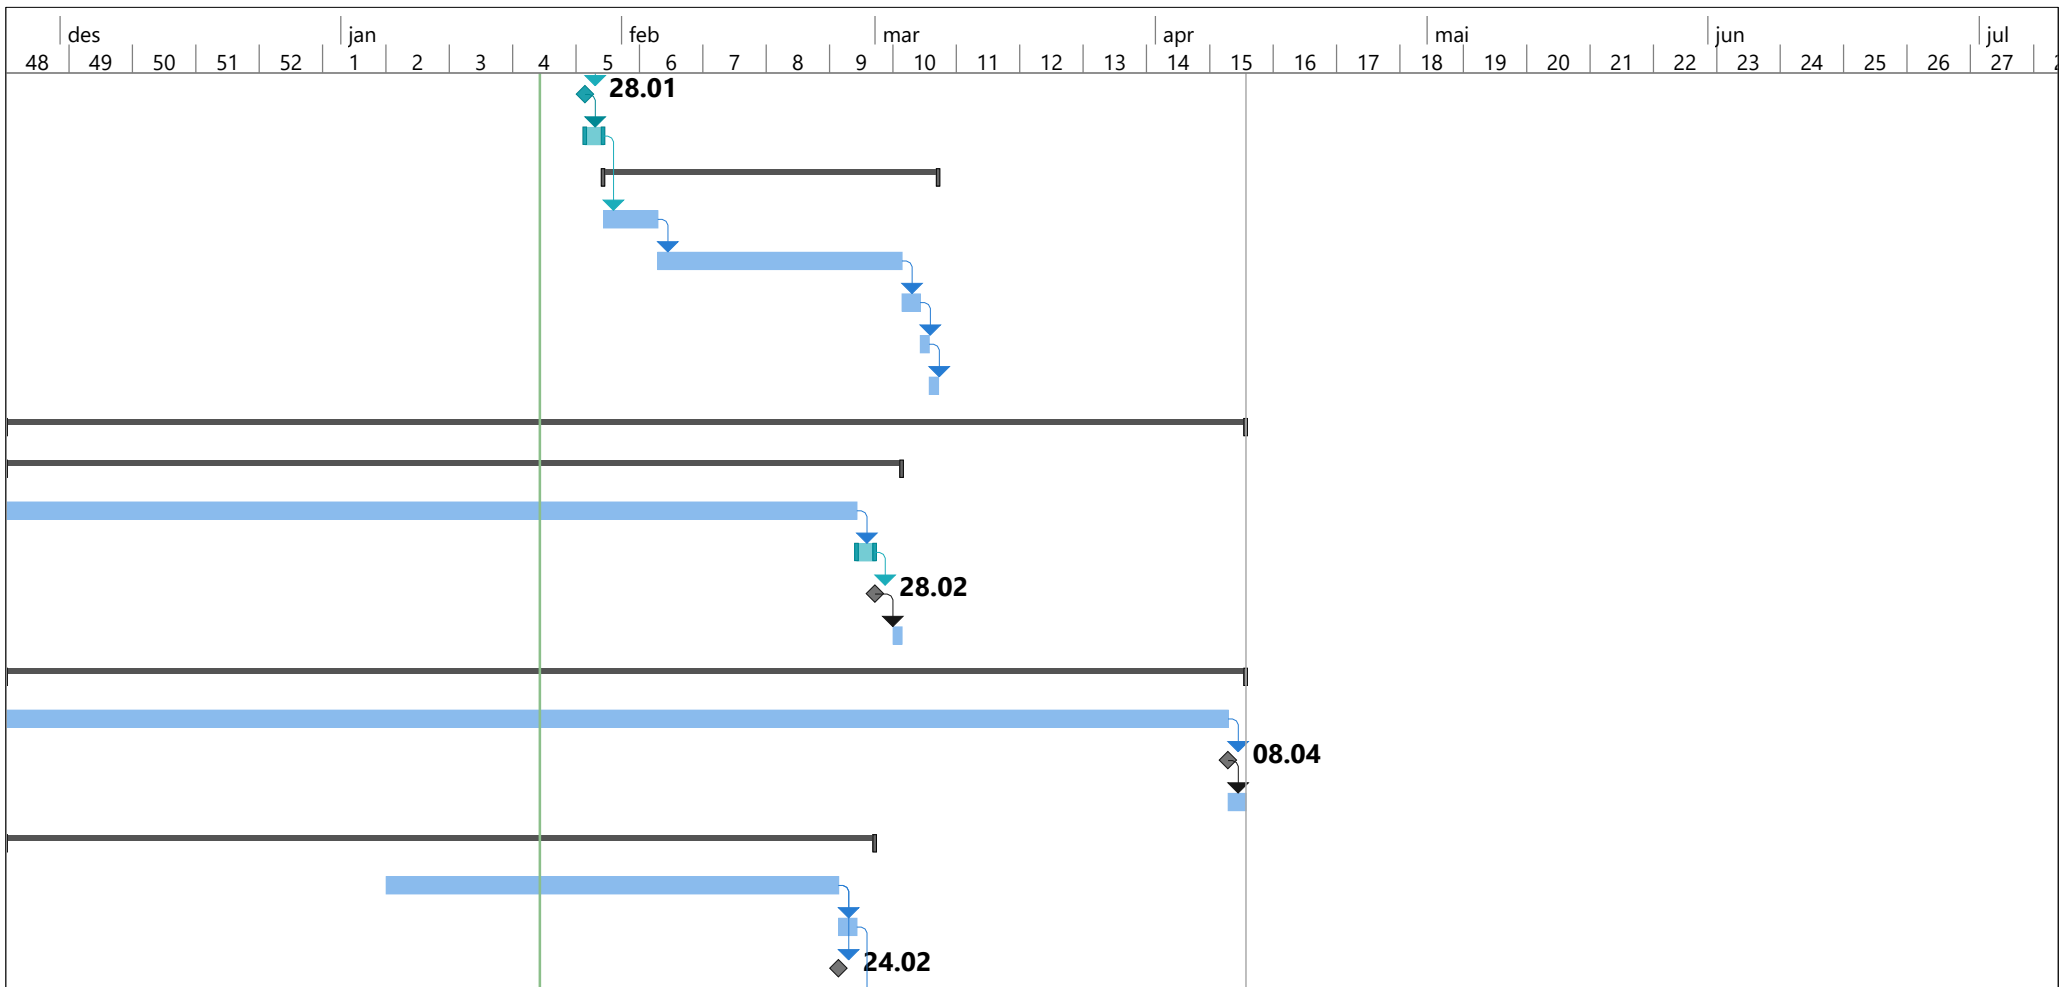

Prosjekt: Overordnet tidsplan re
 Dato: to 23.01.25

Aktivitet		Inaktivt sammendrag		Eksterne aktiviteter	
Deling		Manuell aktivitet		Ekstern milepæl	
Milepæl		Bare varighet		Tidsfrist	
Sammendrag		Manuell sammendragsfremheving		Fremdrift	
Prosjektsammendrag		Manuelt sammendrag		Manuell fremdrift	
Inaktivt aktivitet		Bare start			
Inaktivt milepæl		Bare slutt			

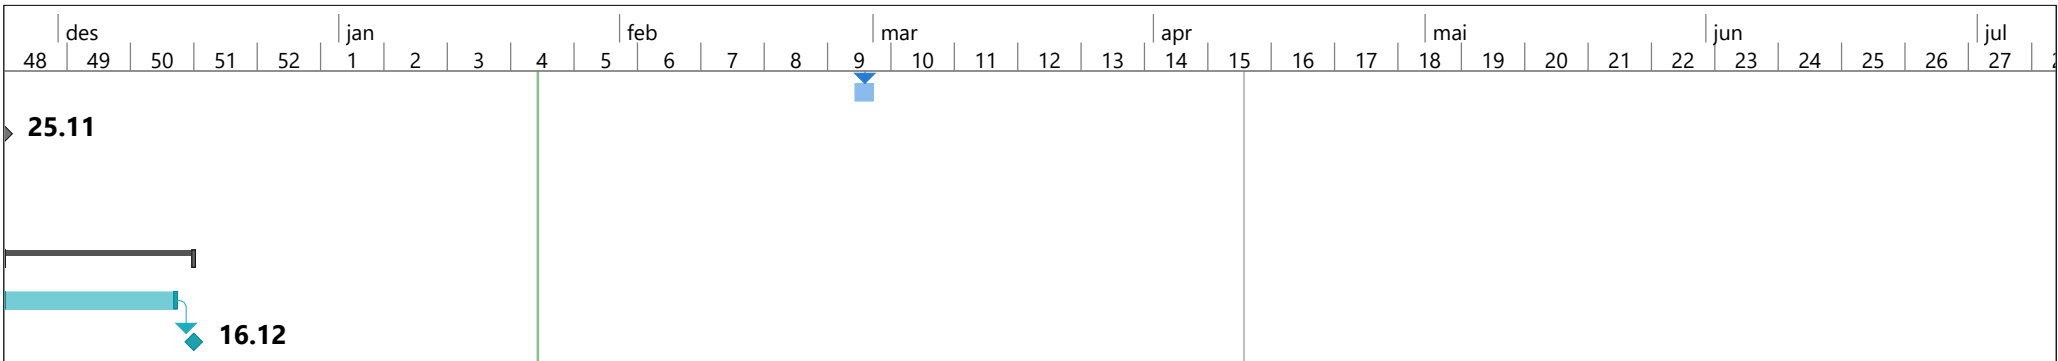

Prosjekt: Overordnet tidsplan re
 Dato: to 23.01.25

Aktivitet		Inaktivt sammendrag		Eksterne aktiviteter	
Deling		Manuell aktivitet		Ekstern milepæl	
Milepæl		Bare varighet		Tidsfrist	
Sammendrag		Manuell sammendragsfremheving		Fremdrift	
Prosjektsammendrag		Manuelt sammendrag		Manuell fremdrift	
Inaktiv aktivitet		Bare start			
Inaktiv milepæl		Bare slutt			
